


ID	Task Mode	Task Name	Duration	Start	Finish	February	May 21	Septemb	Decembe	March 21	July 1	October 1	January 2	May 1	At			
						2/15	4/5	5/24	7/12	8/30	10/18	12/6	1/24	3/13	5/1	6/19	8/7	9/25
1		Program Planning	1 mon	Wed 4/1/15	Tue 4/28/15													
2		Stakeholder Engagement	1 mon	Wed 4/29/15	Tue 5/26/15													
3		Phase I (5 Facilities)	200 days	Wed 5/27/15	Tue 3/1/16													
4		Existing fixture inventory	1 wk	Wed 5/27/15	Tue 6/2/15													
5		Finalize Scope of Work, Costs & Benefits	1 wk	Wed 6/3/15	Tue 6/9/15													
6		Procure equipment	2 mons	Wed 6/10/15	Tue 8/4/15													
7		Installation	150 days	Wed 8/5/15	Tue 3/1/16													
13		Phase I M&V	1 mon	Wed 8/17/16	Tue 9/13/16													
14		Phase II (5 Facilities)	200 days	Wed 3/2/16	Tue 12/6/16													
15		Existing fixture inventory	1 wk	Wed 3/2/16	Tue 3/8/16													
16		Finalize Scope of Work, Costs & Benefits	1 wk	Wed 3/9/16	Tue 3/15/16													
17		Procure equipment	2 mons	Wed 3/16/16	Tue 5/10/16													
18		Installation	150 days	Wed 5/11/16	Tue 12/6/16													
24		Phase II M&V	1 mon	Wed 5/24/17	Tue 6/20/17													
25		Phase III (4 Facilities)	170 days	Wed 12/7/16	Tue 8/1/17													
26		Existing fixture inventory	1 wk	Wed 12/7/16	Tue 12/13/16													
27		Finalize Scope of Work, Costs & Benefits	1 wk	Wed 12/14/16	Tue 12/20/16													
28		Procure equipment	2 mons	Wed 12/21/16	Tue 2/14/17													
29		Installation	120 days	Wed 2/15/17	Tue 8/1/17													
34		Project close out	2 mons	Wed 8/2/17	Tue 9/26/17													

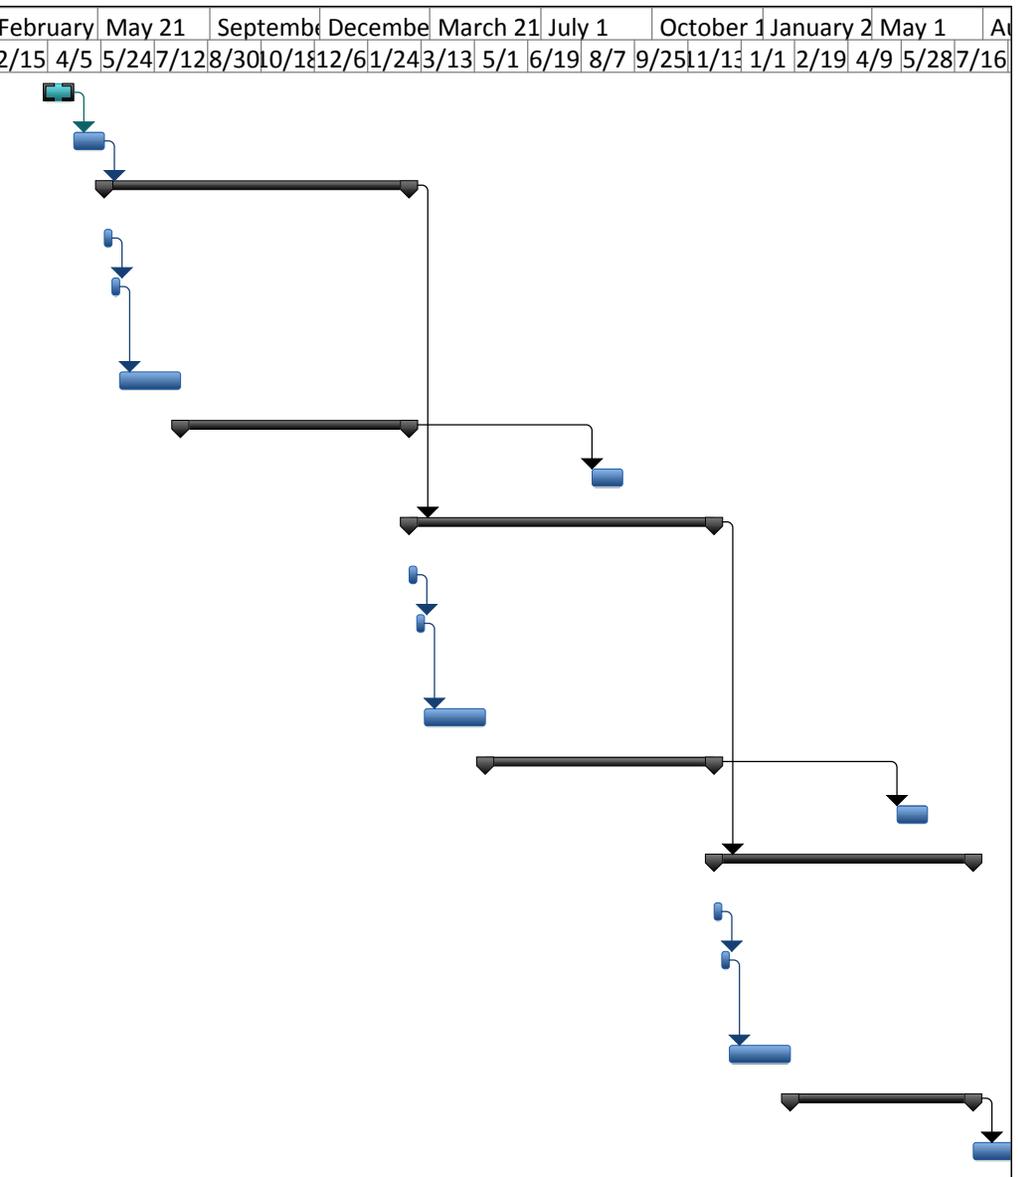

Project: LACMTA - Water Date: Fri 12/12/14	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
