




Sheet 4 - Negro Canyon Restoration Plan - Project G3

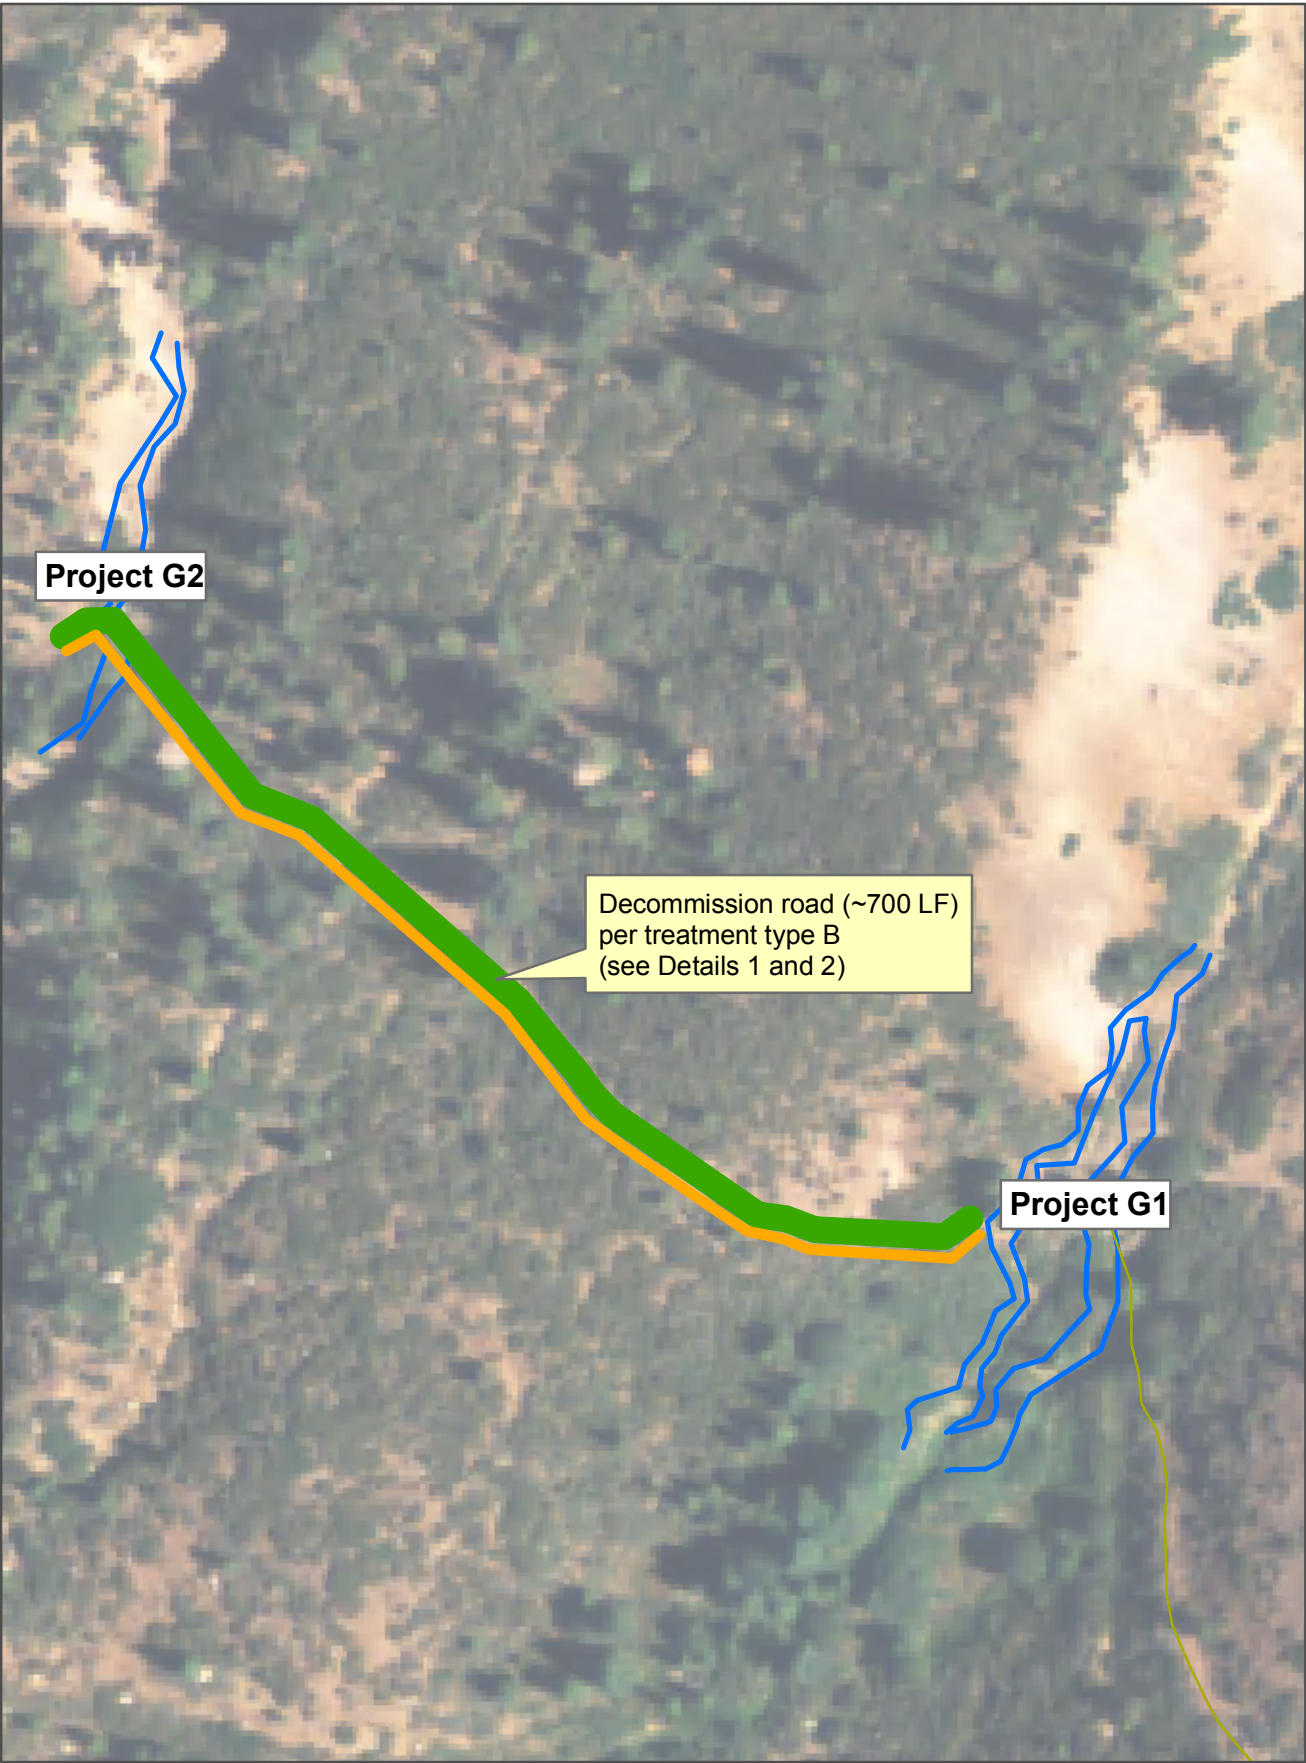

Detail 1. Road decommissioning (Type B)

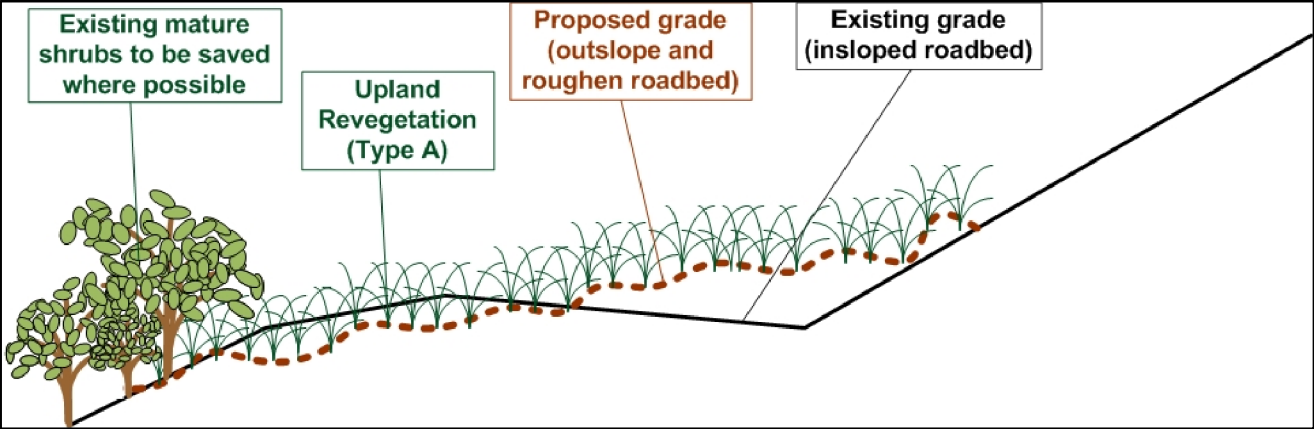

Detail 2. Road decommissioning photo detail

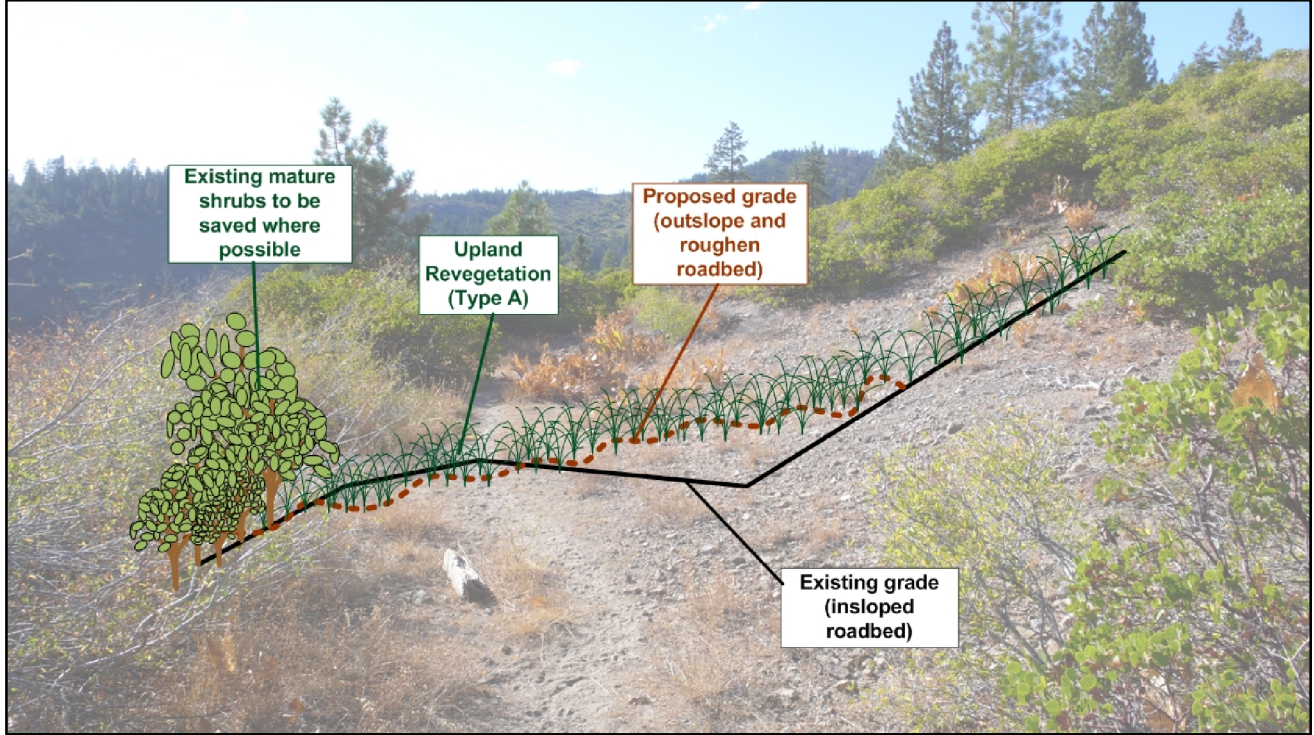

Legend


- Road Decommissioning/Restoration
- Existing Drainages (top banks)
- Pine Needle Wattles

Treatment Area Estimate

Project ID	Length (ft)	Avg width (ft)	Total sq ft	Avg Cut-Fill Depth (ft)	Volume (CY)
G3	700	25	17500	3	1556

Notes

- Design details not to scale.
- Fill material from projects G1 and G2 will be utilized to outslope road.
- Pine needle wattles will be installed downslope of active treatment areas until all bare soil is mulched.
- Road decommissioning could continue further west if desired.



1 inch = 117 feet
