Exhibit I

Crawford/Alvarado Dive Reports

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 16L mile 132.81

DATE AND TIME OF DIVE: 0900 · 2-5-07

PURPOSE OF DIVE:
Seal Stop logs
Install Plug

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
30'	50°	3'

DIVERS NAMES:
Tim Crawford
Martin Alvarado

DIVE TIME: 6

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE:
Sealed Stop log with okum
There was 2' of silt and debri
on Bottom. This is a raised
Turnout with old work damage.
Hard to seal. Water Elevation
has to be lowered.

DATE: 2-5-07

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

WR 34.39

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: Mile 134.94 18L

DATE AND TIME OF DIVE: 0900 1-8-07

PURPOSE OF DIVE: Check and Seal gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	50°	3'

DIVERS NAMES: Tim Crawford

Martin Alvarado

DIVE TIME: 6

TOTAL MAN HOURS DIVING: 6 HRS

DESCRIPTION OF DIVE:

A - Barrel Leaked Sealed with oKum

B - Barrel Sealed O.K.

Four to Five Foot of silt in Front of Both gate's

DATE: 1-8-07

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

(WR 34.09)

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION	DATE AND TIME OF DIVE
# 75000081171 9 L mile 120.77) and (# 75000081172 11 L mile 124.18	1-2-07 0900

PURPOSE OF DIVE

Check & Seal Gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
15'	50°	3'

DIVERS NAMES

Tim Crawford

Martin Alvarado

DIVE TIME 6

TOTAL MAN HOURS DIVING 6

DESCRIPTION OF DIVE

9 L - B Barrel Leaked Sealed with okum
A Barrel ok

11 L - A Barrel Leaked Sealed with okum
B - ok - new gate.

DATE	DIVE SUPERVISOR'S SIGNATURE
1-2-07	Tim Wd

DWR 34.29

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT #7500008092?

DIVE LOCATION

14R mile 135 96

DATE AND TIME OF DIVE

10:00 12-26-06

PURPOSE OF DIVE

Check & seal gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
15'	45°	3'

DIVERS NAMES

Tim Crawford

Martin Alvarado

DIVE TIME

6

TOTAL MAN HOURS DIVING 6

DESCRIPTION OF DIVE

Both gate's and guide's are in good condition, gate's sealed no problem's. 1' of silt in front of gate's

DATE

12-26-06

DIVE SUPERVISOR'S SIGNATURE

Tim Crawford

DWR 34.39

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT # 7500008053 6

DIVE LOCATION

DWP 29 R mile 16.7 84

DATE AND TIME OF DIVE

12/18/06 0800

PURPOSE OF DIVE

check & Seal gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
15'	50°	3'

DIVERS NAMES

Tim Crawford

MARTIN ALVARADO

DIVE TIME

6

TOTAL MAN HOURS DIVING 6

DESCRIPTION OF DIVE

Both A & B Barrel leaked
Sealed with dkum
Both gate's Hard to close
All the way, Stem's & guides
in good condition, 1' to 2' of
Silt on Bottom

DATE

12-18-06

DIVE SUPERVISOR'S SIGNATURE

Tim

WR 34.29

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: Mile 132.81 16 L

DATE AND TIME OF DIVE: 12-11-06 0900

PURPOSE OF DIVE: check & seal gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	50°	3'

DIVERS NAMES: Tim Crawford
Martin Alvarado

DIVE TIME: 6

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE:

Both A & B Barrels Sealed
Gate's are in good condition
6" of Silt Built up in
front of gate's

DATE: 12-11-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

WR 3439

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION #750000 80335 #750000 80336

5L mile 111.93 AND 8L mile 117.5

DATE AND TIME OF DIVE

900

12-4-06 11:00

PURPOSE OF DIVE

Check and Seal gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	50°	2'

DIVERS NAMES

Tim Crawford

MARTIN Alvarado

DIVE TIME

3

TOTAL MAN HOURS DIVING 6

DESCRIPTION OF DIVE

5L - B Barrel leaks, Sealed with okum, A Barrel ok Both gate's in good condition.

8L - A Barrel leaks sealed with okum wedge's need Adjusting gate won't Close all the way.

C- Barrel Leaks Sealed with okum

B-Barrel ok

DATE

12-4-06

DIVE SUPERVISOR'S SIGNATURE

Tim

IWR 34.29

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: Dos Amigos P.P.

DATE AND TIME OF DIVE: 11-28-06 0400

PURPOSE OF DIVE: Inspect TRASh RACK's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
30'	50°	3'

DIVERS NAMES: Tim Crawford

MARTIN ALVARADO

DIVE TIME: 3

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE

Removed HAND RAIL FROM BOTTOM

(See ATTACHED DRAWING)

11-28-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

VR 3429

Definition's - only the outside Bars on each Grate are Ba

Thin - 1/16" to 1/4" Thick

Good - 1/4" to 1/2" Thick

Broken - Bar is Bent or Broken off in a section

Missing Bar is completly gone

(11-28-06)
TC

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: Mile 130 85 14. Left

DATE AND TIME OF DIVE: 0900 11-27-06

PURPOSE OF DIVE: Seal gate's

DEPTH OF DIVE: 15'

WATER TEMPERATURE: 50°

WATER VISIBILITY: 5'

DIVERS NAMES: Tim Crawford
MARTIN ALVARADO

DIVE TIME: 3

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE:

Gate's B, C, D, All Leak we sealed with okum

The wedge's and or limit switche's weed to Be Adjusted gate's will not go all the way DOWN.

DATE: 11-27-06

DIVE SUPERVISOR'S SIGNATURE: Tim Lyd

DWR 3409

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: Mi 160.45 25 R

DATE AND TIME OF DIVE: 11-13-06 0900

PURPOSE OF DIVE: Check & Seal Gates

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	55°	5'

DIVERS NAMES: Tim Crawford

~~Sam~~

Martin Alvarado

DIVE TIME: 2 HRS

TOTAL MAN HOURS DIVING: 4 HRS

DESCRIPTION OF DIVE:

A Barel - Stem is Bent, Gate is in Poor condition several Rusted Area's. Top Stem Guide is loose and off the wall. Gate Leaks had to seal with okum.

B Barel - Good condition Small leak on top Seal.

DATE: 11-13-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

DWR 3429

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 90.14 Right Bank.

DATE AND TIME OF DIVE: 11:00 11-7-06

PURPOSE OF DIVE: Inspect For Damage

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
30'	60°	5'

DIVERS NAMES: Tim Crawford
Martin Alvarado

DIVE TIME: ~~3~~ HH

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE:

9 Panels down stream From Ladder we Found A 2" gap At the invert. 15' Long. Appears to be taking water. NO Damage to any Panels.

DATE: 11-7-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

DWR 34.39

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION	DATE AND TIME OF DIVE
88, 50 Southside Pole line 1 Bridge	0900 11-7-06

PURPOSE OF DIVE

Inspect DAMAGE

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
30'	60°	5'

DIVERS NAMES

Tim Crawford

Martin Alvarado

DIVE TIME 3

TOTAL MAN HOURS DIVING 6

DESCRIPTION OF DIVE

Inspect DAMAGE liner

(See DRAWING)

DATE	DIVE SUPERVISOR'S SIGNATURE
11-7-06	Tim Crawford

DWR 34.29

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 84,50

DATE AND TIME OF DIVE: 11-6-06 0900

PURPOSE OF DIVE: Inspect Liner

DEPTH OF DIVE: 30'

WATER TEMPERATURE: 60°

WATER VISIBILITY: 5'

DIVE TIME: 6 HR

DIVERS NAMES:
Tim Crawford
Martin Alvarado

TOTAL MAN HOURS DIVING: 12

DESCRIPTION OF DIVE:
Inspect Liner on left Bank, From 2nd set of Steps to the Bridge. Found No Damage.

Inspect Liner on Right Bank From visual Damage to top two Panels 5 Panels wide down to invert. (see Drawing)

DATE: 11-6-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

DWR 34.29

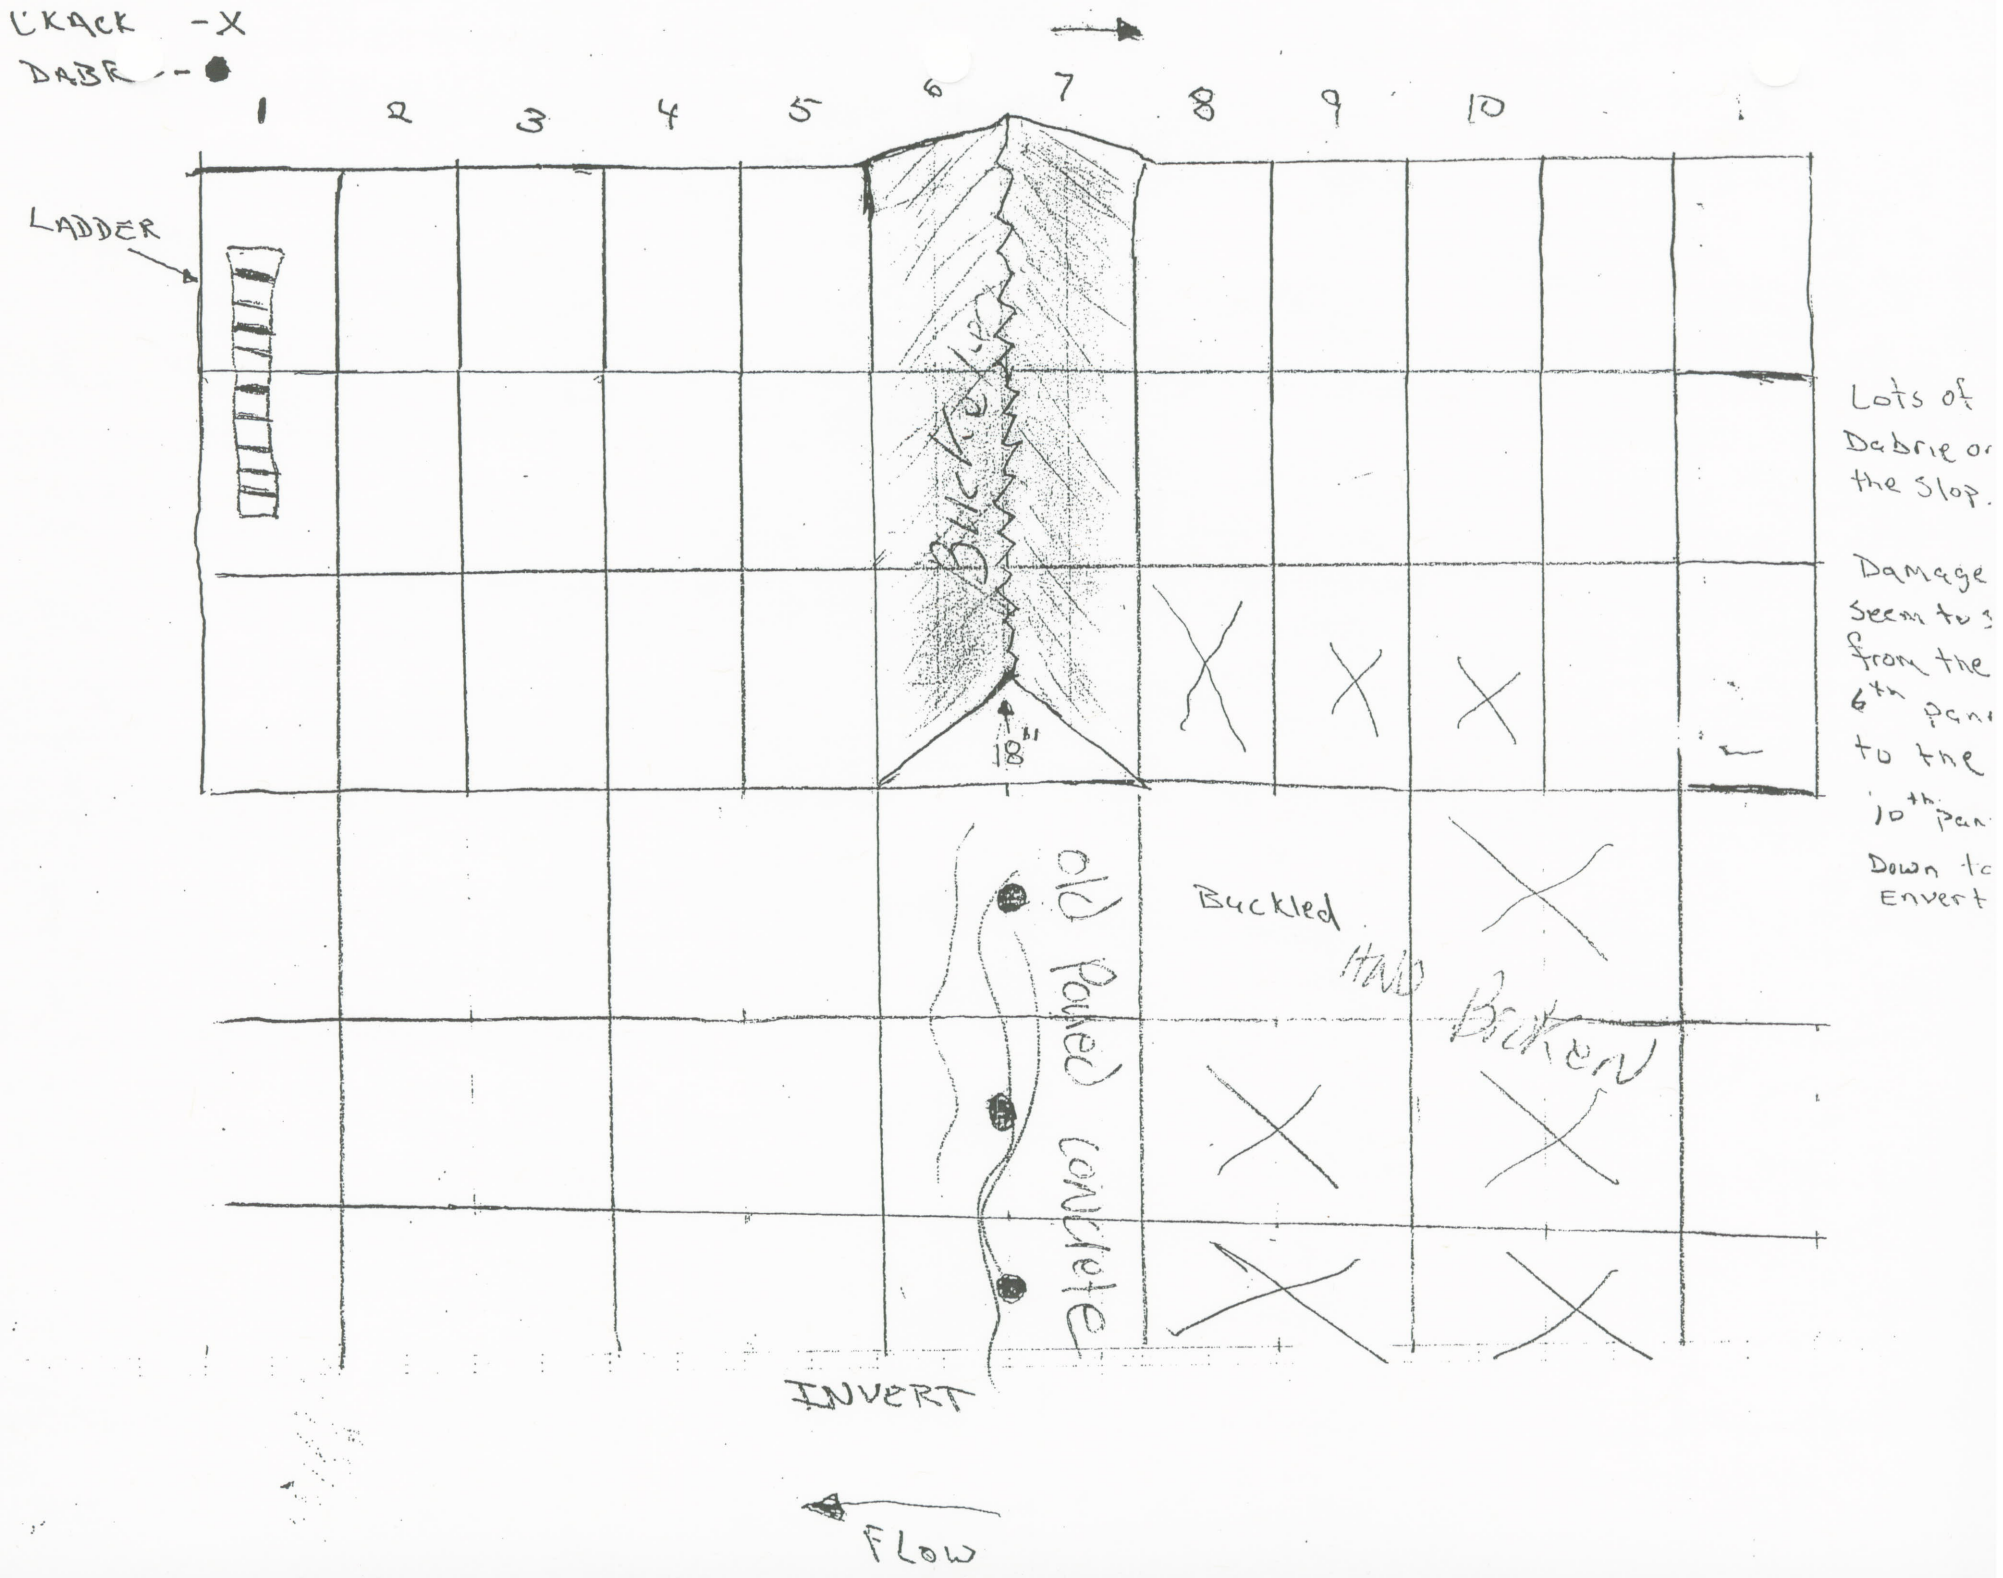

Lots of Dabrie on the Slop.

Damage Seem to s from the 6th pan to the 10th pan Down to Envert

up Stream → right bank

Poline 1 Brg →

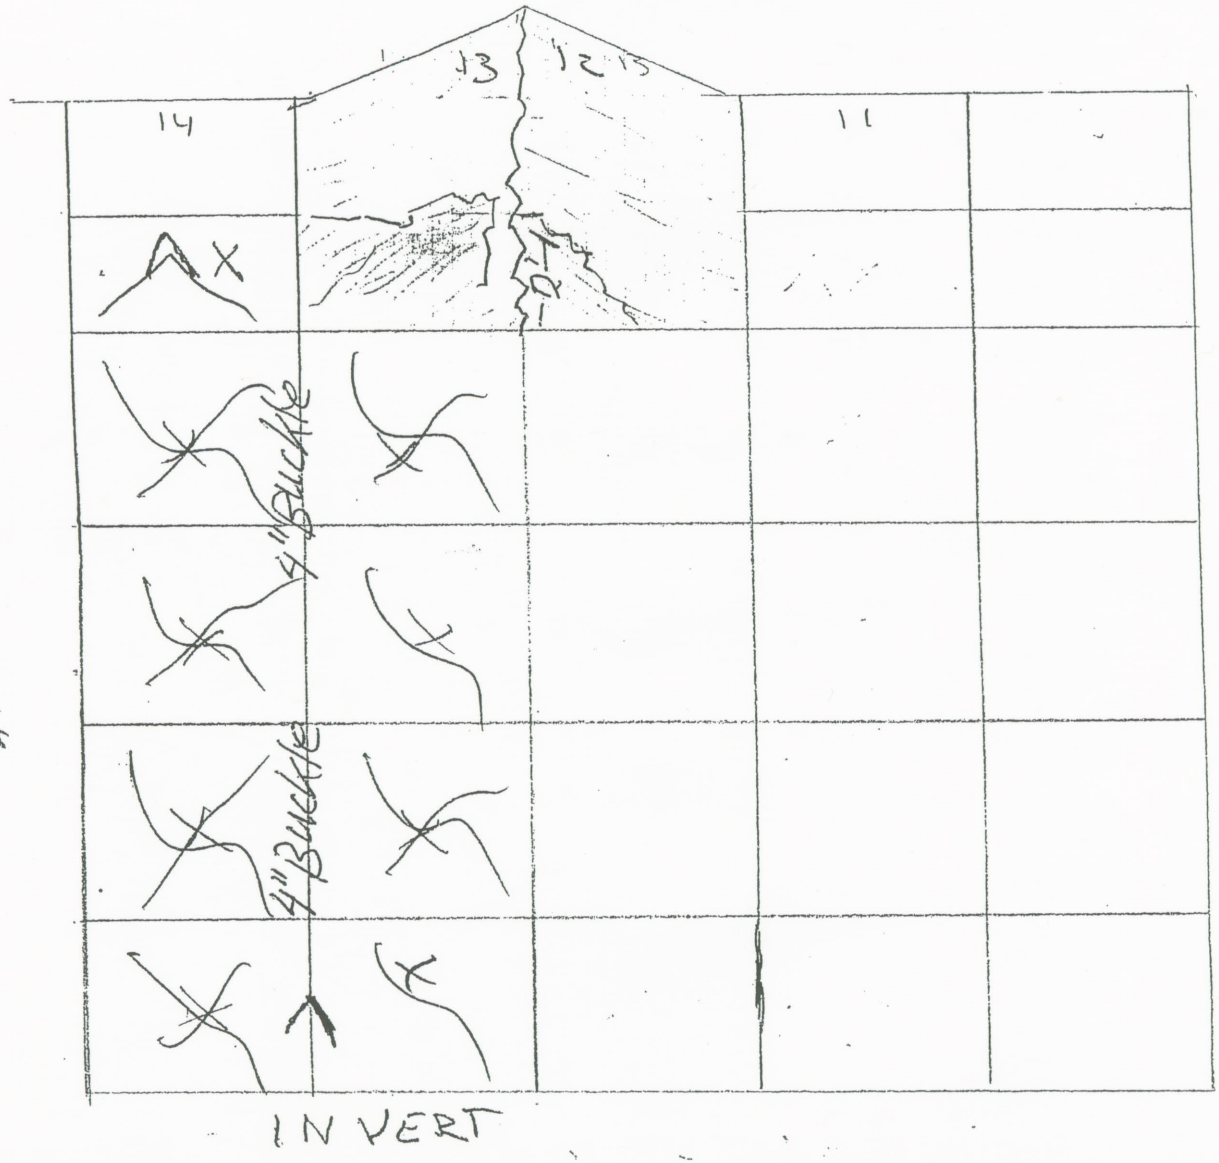

Bridge

-Λ

ed -X

→

on right bank
Pole line Brg. is
; surface buckel
op liner down to

f this same panel
cking out of water

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 88.30

DATE AND TIME OF DIVE: 10-31-06 900 AM

PURPOSE OF DIVE: Check For Damage

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
30'	60	5'

DIVERS NAMES: Tim Crawford
Martin Alvarado

DIVE TIME: 6

TOTAL MAN HOURS DIVING: 12

DESCRIPTION OF DIVE:

started at Ladder, Both Side's. 43 Pawels From the Ladder on the left Bank is some old Damage visiable From the Top. Under water the Panel is Buckeled All the way Down to the invert. (see Drawing) All other Panel's Look good no Damage Both Side's we looked at 100 Pawels, From Ladder to Pipeline, Both Side's, From invert to surface.

DATE: 11-1-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

DWR 34.29

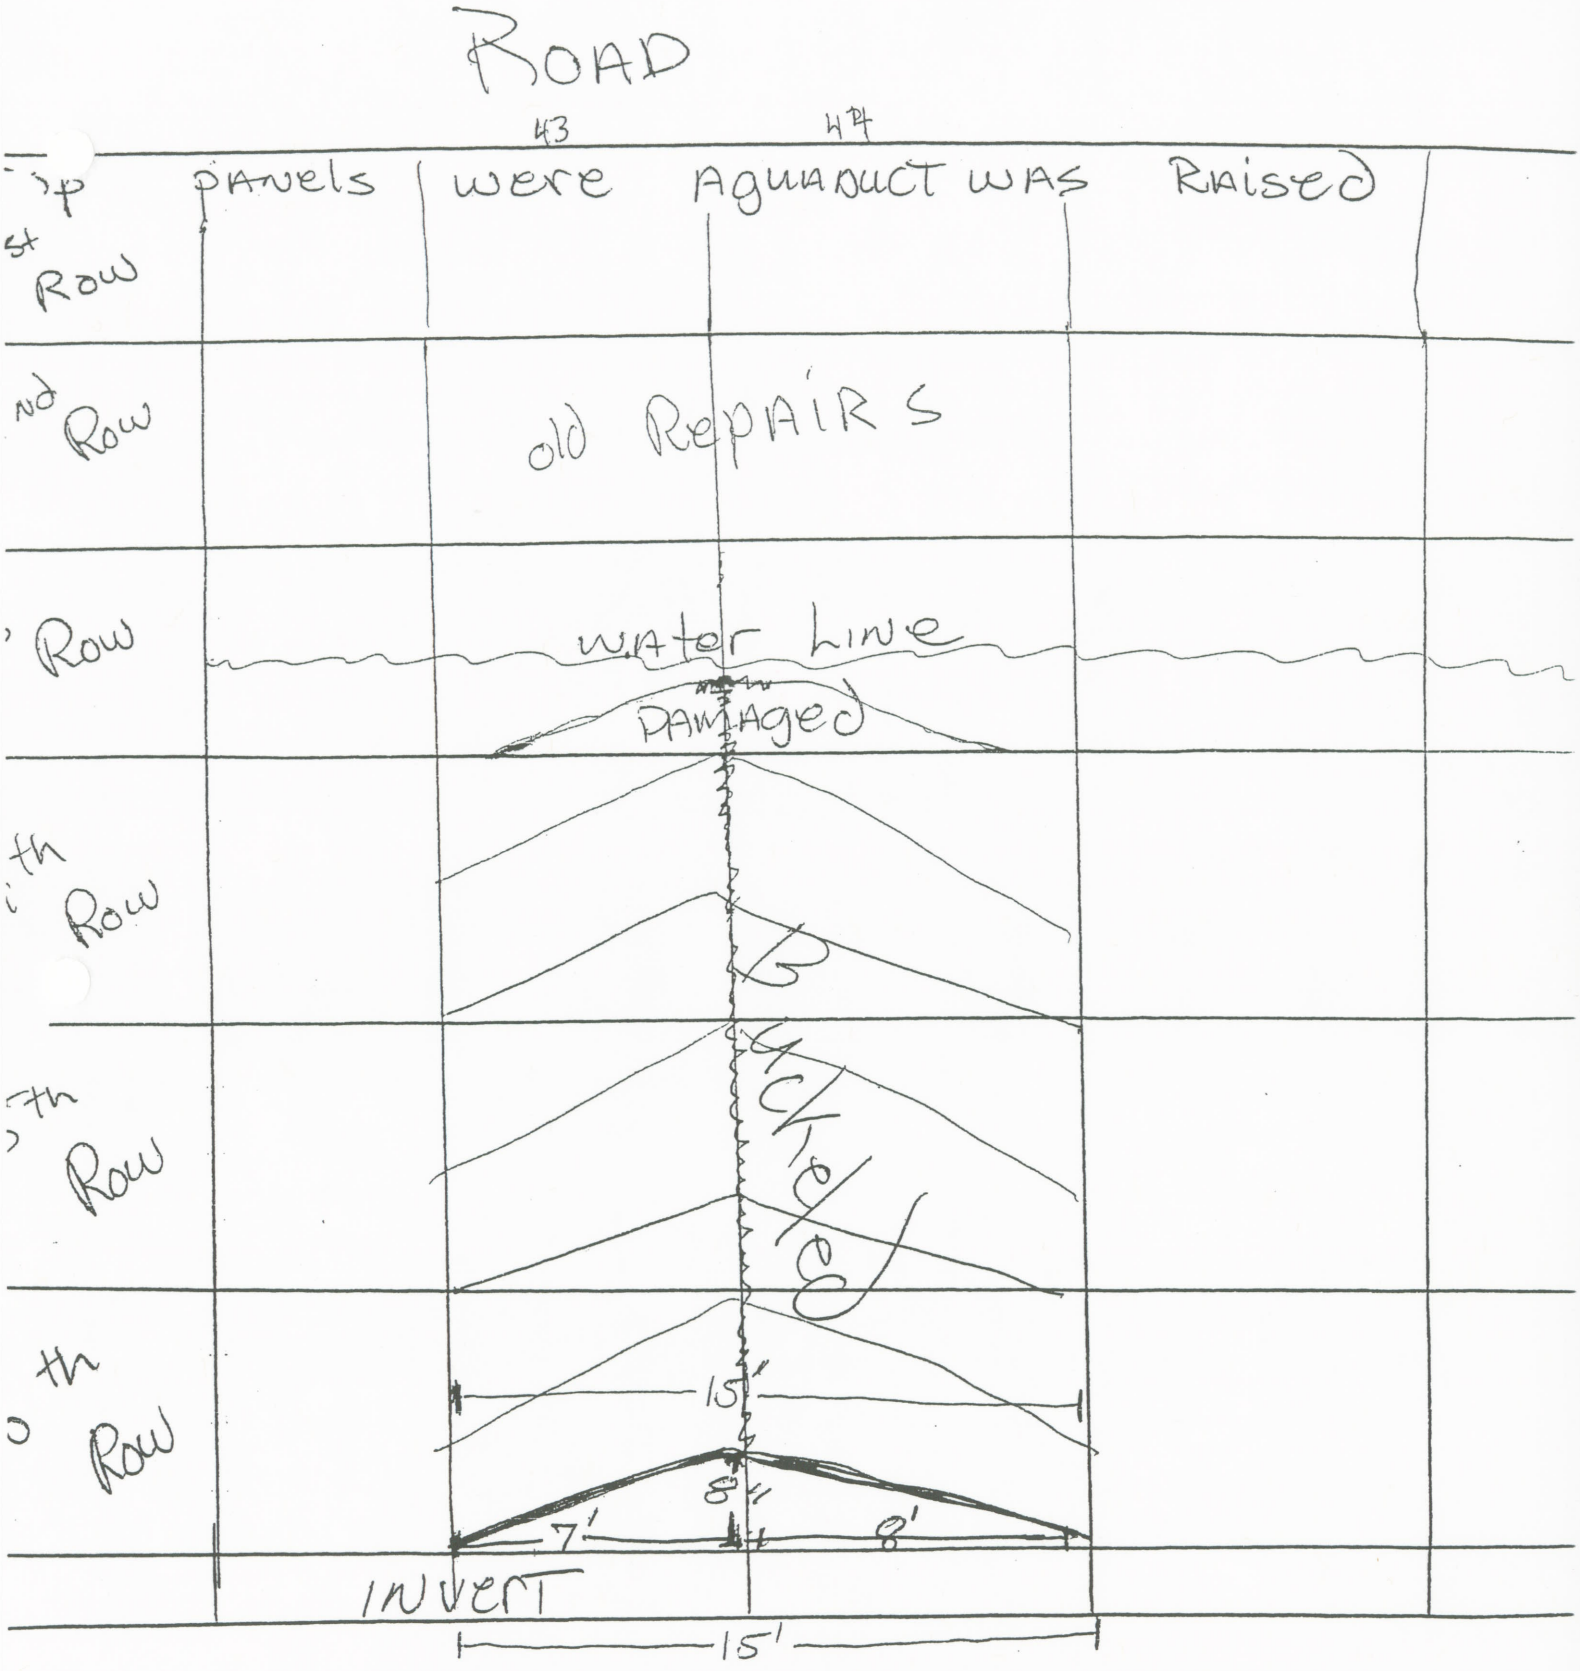

BOTTOM

8" Gap at invert
1" to 2" Gap all Along TOP of Buckel.



TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 88.30

DATE AND TIME OF DIVE: 10-31-06 900 AM

PURPOSE OF DIVE: Check For Damage

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
30'	60	5'

DIVERS NAMES: Tim Crawford
Martin Alvarado

DIVE TIME: 6

TOTAL MAN HOURS DIVING: 12

DESCRIPTION OF DIVE:

started at Ladder, Both Side's. 43 Pawels From the Ladder on the left Bank is some old Damage visiable From the Top. under water the Panel is Buckeled all the way DOWN to the invert. (see DRAWING) All other Pawel's Look good no DAMAGE Both Side's we looked at 100 Pawels From Ladder to Pipeline, Both Side's, From invert to surface.

11-1-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

IWR 38.50

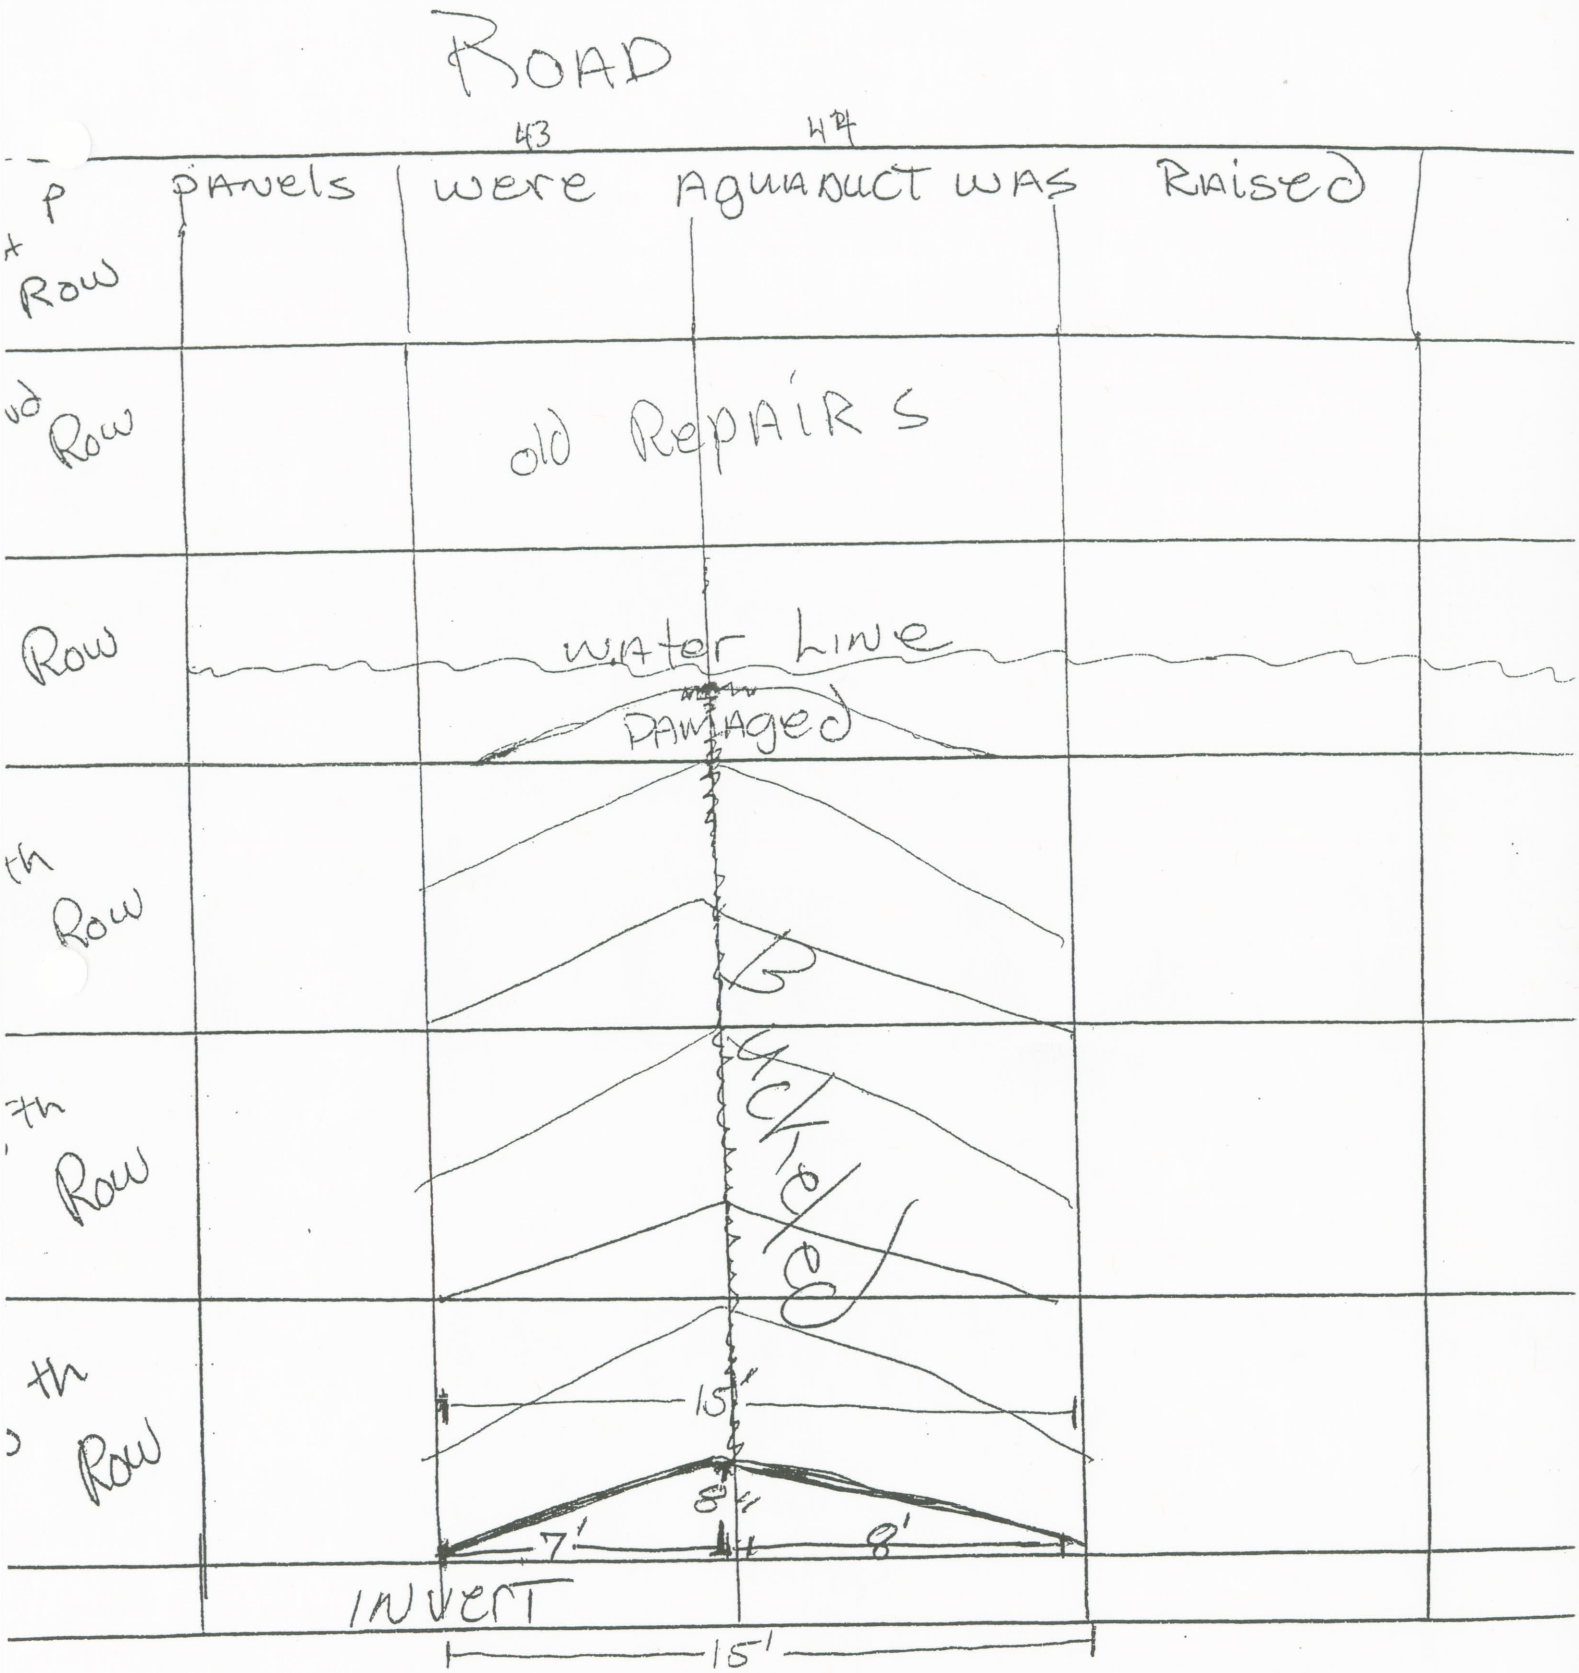

BOTTOM

8" Gap at invert
1" to 2" Gap all Along TOP of Buckel.

Buckel

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 20 L mile 137.11

DATE AND TIME OF DIVE: 0900 10-30-06

PURPOSE OF DIVE: Check & Seal gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	60°	5'

DIVERS NAMES: Tim Crawford
MARTIN Alvarado

DIVE TIME: 3

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE:

All gate's closed AND Sealed

No problem's

2' of silt on Bottom

DATE: 10-30-06

DIVE SUPERVISOR'S SIGNATURE: Tim Crawford

DWR 34.09

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 13L - 129.88 AND 17L 133.81

DATE AND TIME OF DIVE: 0900 10-23-06

PURPOSE OF DIVE: Seal leaks

DEPTH OF DIVE: 15'

WATER TEMPERATURE: 60°

WATER VISIBILITY: 5'

DIVERS NAMES: Tim Crawford
Martin Alvarado

DIVE TIME: 3

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE:

13L - A Barrel leaked sealed with okum -

17L - B Barrel leaked, could not seal?, small leak

DATE: 10-23-06

DIVE SUPERVISOR'S SIGNATURE: Tim

DWR 3429

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION

Mile 147.02 26 L

DATE AND TIME OF DIVE

0900 10-2-06

PURPOSE OF DIVE

Check and Seal gates

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	60°	3'

DIVERS NAMES

Tim Crawford

MARTIN

DIVE TIME

3 HRS

TOTAL MAN HOURS DIVING

DESCRIPTION OF DIVE

B - Barrel 66" gate - Leaks Had to Seal with okum on TOP.

A Barrel 30" Sealed

DATE

10-20-06

DIVE SUPERVISOR'S SIGNATURE

Tim

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION: 15L 131.70

DATE AND TIME OF DIVE: 0900 10-16-06

PURPOSE OF DIVE: Check & Seal

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	60	10'

DIVERS NAMES: Tim Crawford
Martin Alvarado

DIVE TIME: 3

TOTAL MAN HOURS DIVING: 6

DESCRIPTION OF DIVE: Gate's closed No problem's
30" Gate is new Sealed tight

DATE: 10-16-06

DIVE SUPERVISOR'S SIGNATURE: Tim Lyd

TECHNICAL UNDERWATER INSPECTION TEAM

DIVE REPORT

DIVE LOCATION

Mile 161.60 26R

DATE AND TIME OF DIVE

10-10-06 0900

PURPOSE OF DIVE

Check & Seal Gate's

DEPTH OF DIVE	WATER TEMPERATURE	WATER VISIBILITY
20'	60°	3'

DIVERS NAMES

Tim Crawford

Martin Alvarado

DIVE TIME

3

TOTAL MAN HOURS DIVING 6

DESCRIPTION OF DIVE

Gate's Sealed no Problem's

	DIVE SUPERVISOR'S SIGNATURE
10-10-06	Tim Crawford
