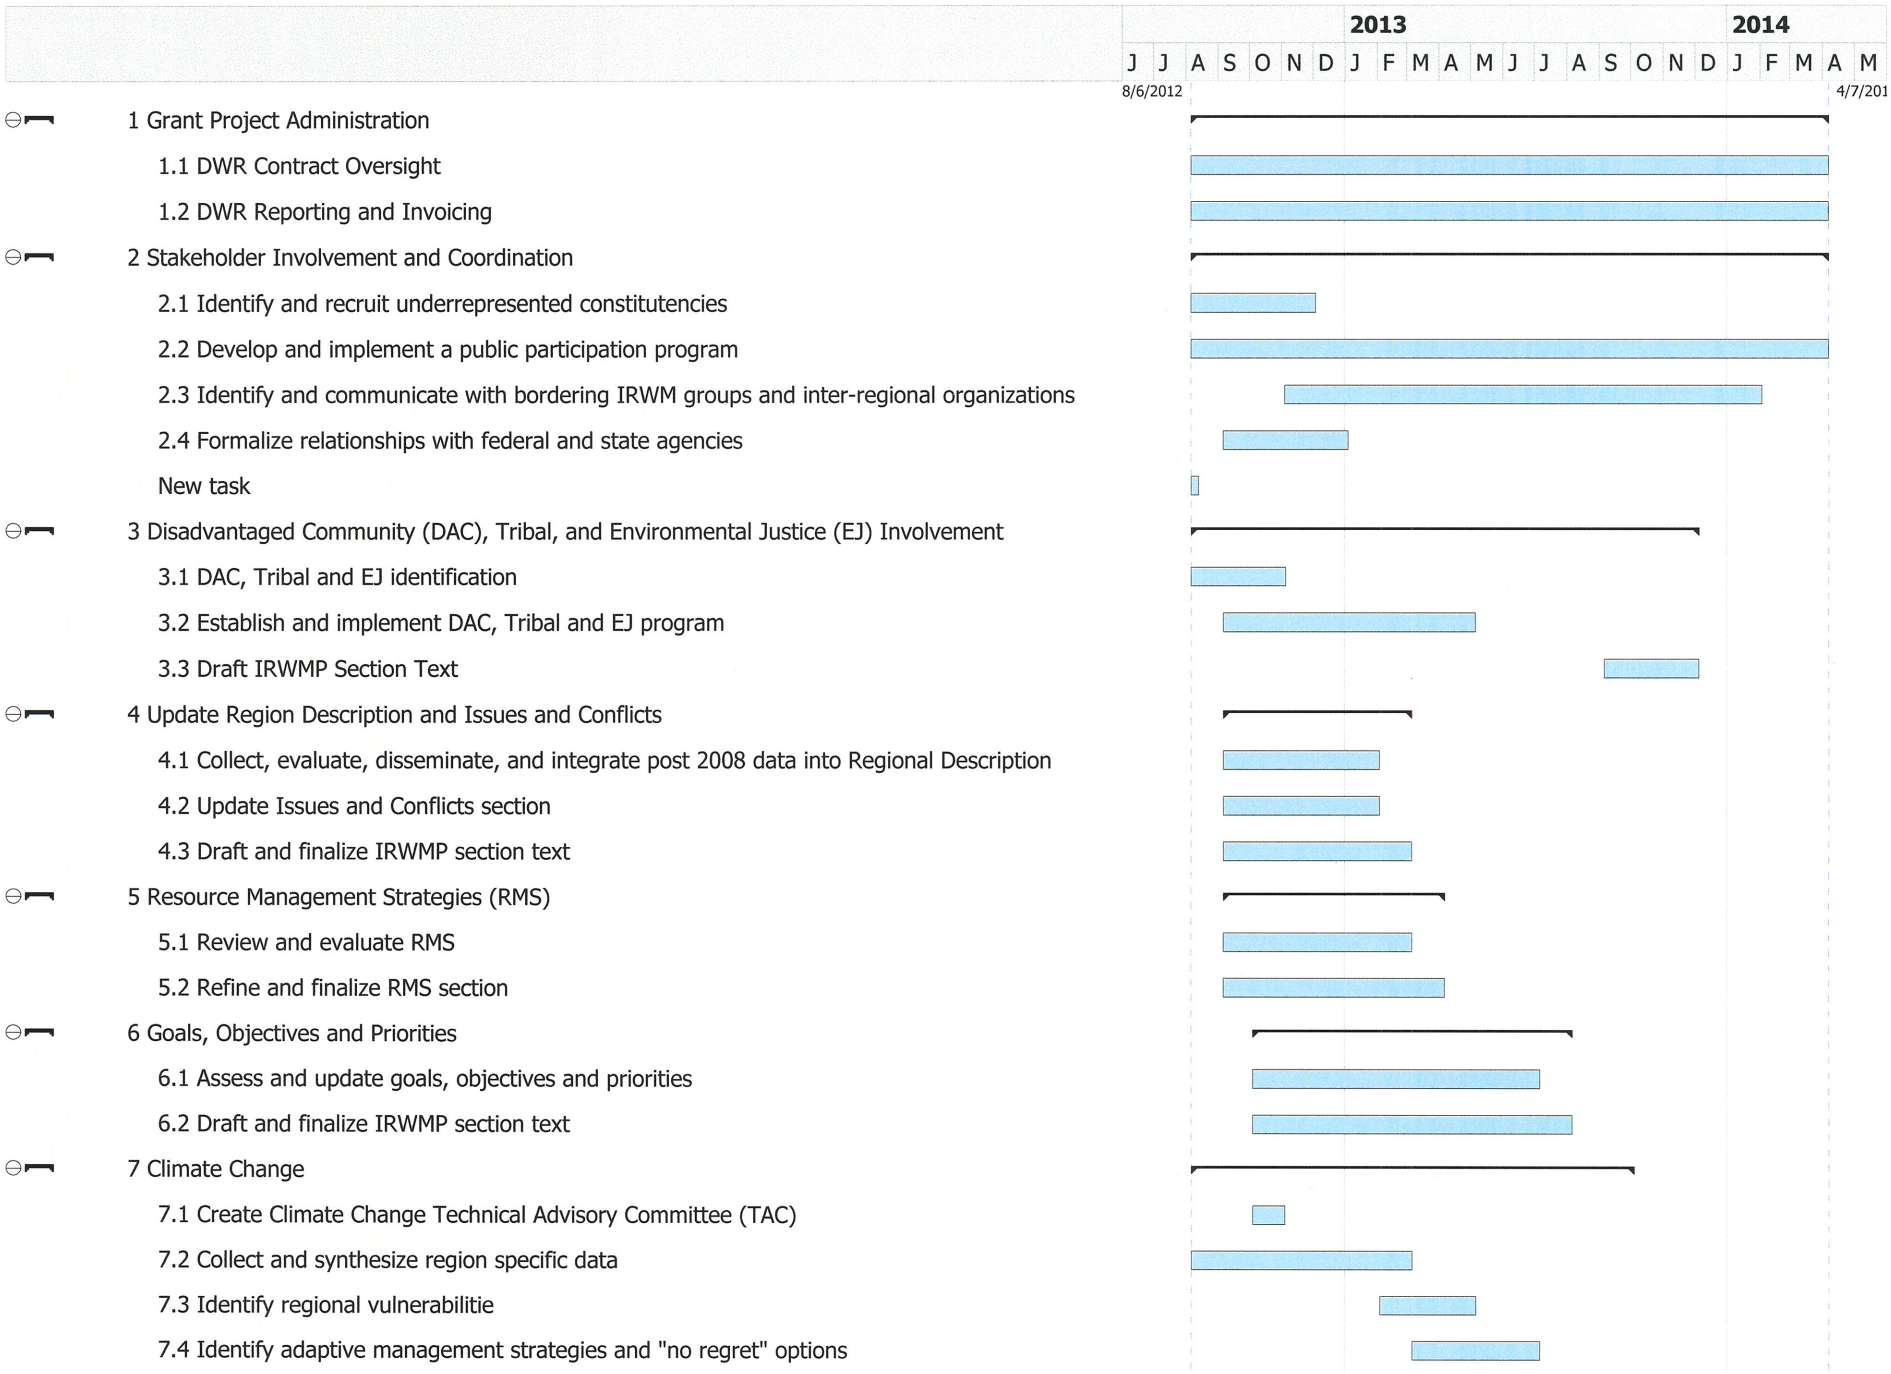
2013
2014
J J A S O N D J F M A M J J A S O N D J F M A M
8/6/2012
4/7/201
1 Grant Project Administration
1.1 DWR Contract Oversight
1.2 DWR Reporting and Invoicing
2 Stakeholder Involvement and Coordination
2.1 Identify and recruit underrepresented constitutencies
2.2 Develop and implement a public participation program
2.3 Identify and communicate with bordering IRWM groups and inter-regional organizations
2.4 Formalize relationships with federal and state agencies
New task
3 Disadvantaged Community (DAC), Tribal, and Environmental Justice (EJ) Involvement
3.1 DAC, Tribal and EJ identification
3.2 Establish and implement DAC, Tribal and EJ program
3.3 Draft IRWMP Section Text
4 Update Region Description and Issues and Conflicts
4.1 Collect, evaluate, disseminate, and integrate post 2008 data into Regional Description
4.2 Update Issues and Conflicts section
4.3 Draft and finalize IRWMP section text
5 Resource Management Strategies (RMS)
5.1 Review and evaluate RMS
5.2 Refine and finalize RMS section
6 Goals, Objectives and Priorities
6.1 Assess and update goals, objectives and priorities
6.2 Draft and finalize IRWMP section text
7 Climate Change
7.1 Create Climate Change Technical Advisory Committee (TAC)
7.2 Collect and synthesize region specific data
7.3 Identify regional vulnerabilitie
7.4 Identify adaptive management strategies and "no regret" options

7.4 Identify adaptive management strategies and "no regret" options

7.5 Public outreach and education

7.6 Draft and Finalize IRWMP Section Text

8 Relation to water and landuse planning

8.1 Water planning

8.2 Landuse planning

8.3 Update to existing plan

9 Project Application, Development and Review

9.1 Refine project application and make available online

9.2 Revised approach to project identification and development

9.3 Integrate EJ constituent needs into project development process

9.4 Develop highly ranked projects to sufficient level for inclusion in the plan

9.5 Project review: revise Project Rating System and prioritize projects

9.6 Draft and Finalize IRWMP section text

10 Finance

10.1 Evaluate the current financial condition of the Yuba Region IRWMP

10.2 Research available funding sources

10.3 Finalize and adopt new section text

11 Impacts and Benefits

11.1 Identify impacts and benefits of IRWMP Implementation

11.2 Develop a method of tracking impacts and benefits as the IRWMP is implemented

11.3 Draft and finalize IRWMP section text

12 Plan and Project Performance

12.1 Develop IRWMP-level performance measures

12.2 Develop Project- level performance measures

12.3 Define responsibility and frequency of plan and project performance review

12.4 Draft and finalize IRWMP section text

13 Data Management

13.1 Collect and evaluate post 2008 data

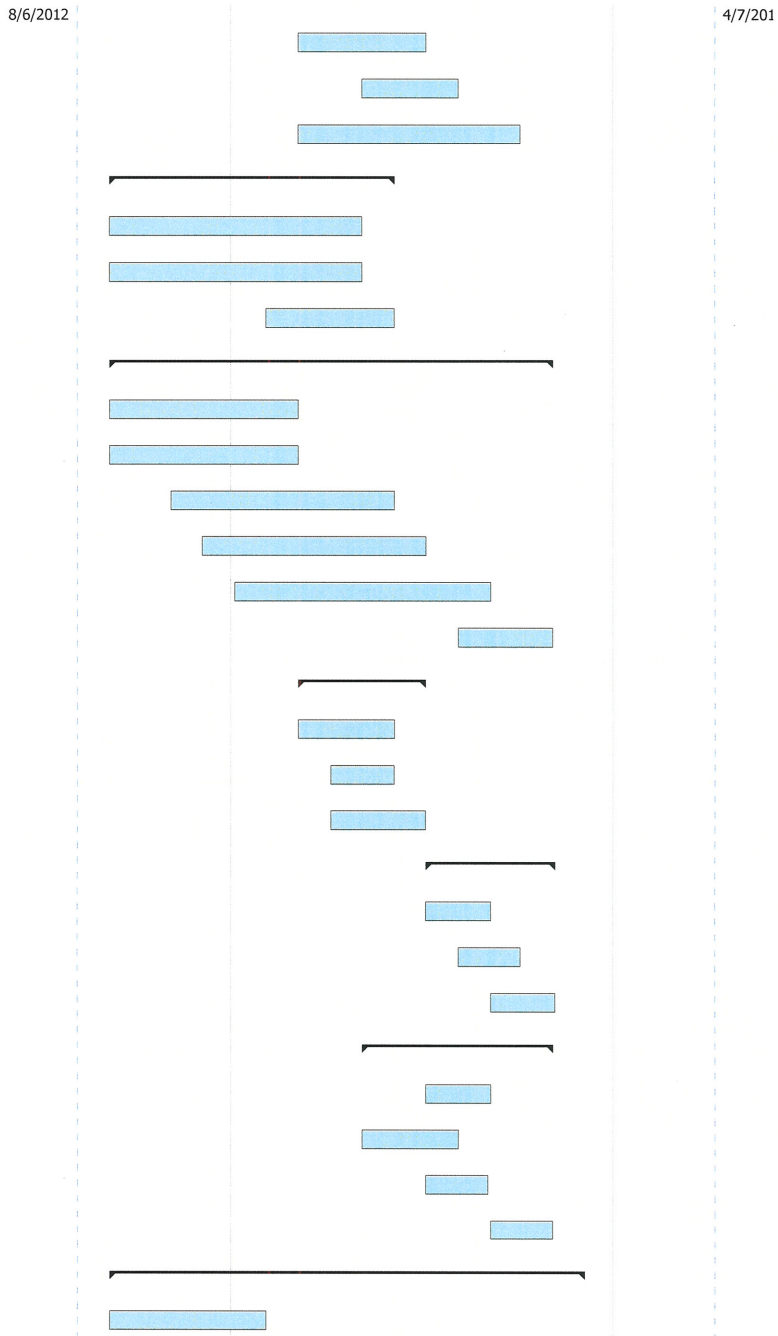

13.2 Coordinate with and update Sacramento

13.3 Website Development

13.4 Develop criteria for collecting and providing data to the IRWM and state databases

13.5 Draft and finalize IRWMP section text

14 Task Analysis

14.1 Describe data information sources used to support IRWMP preparation

14.2 Describe methodologies used to analyze technical information and datasets

14.3 Draft and finalize IRWMP section text

15 Formalize IRWMP Governance

15.1 Review governance options used by IRWM options throughout the state

15.2 Review Yuba IRWMP governance needs and state requirements

15.3 Select and implement governance option

16 IRWMP Preparation

16.1 Develop maps, graphics and identify format for integration into existing document

16.2 Assembly of final document and RWMG review and revision
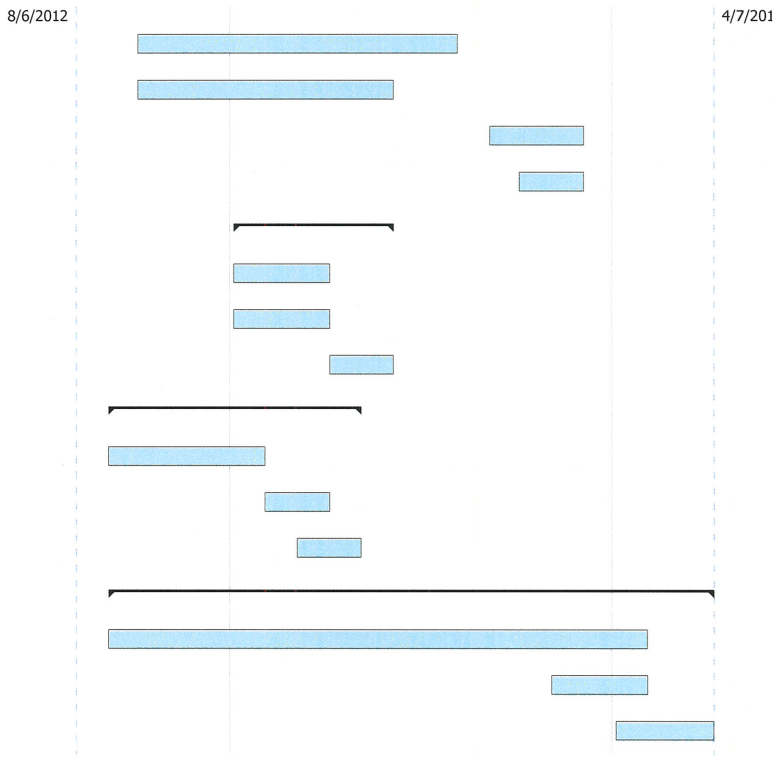
16.3 Adopt the revised IRWMP
