Update 2013 Schedule

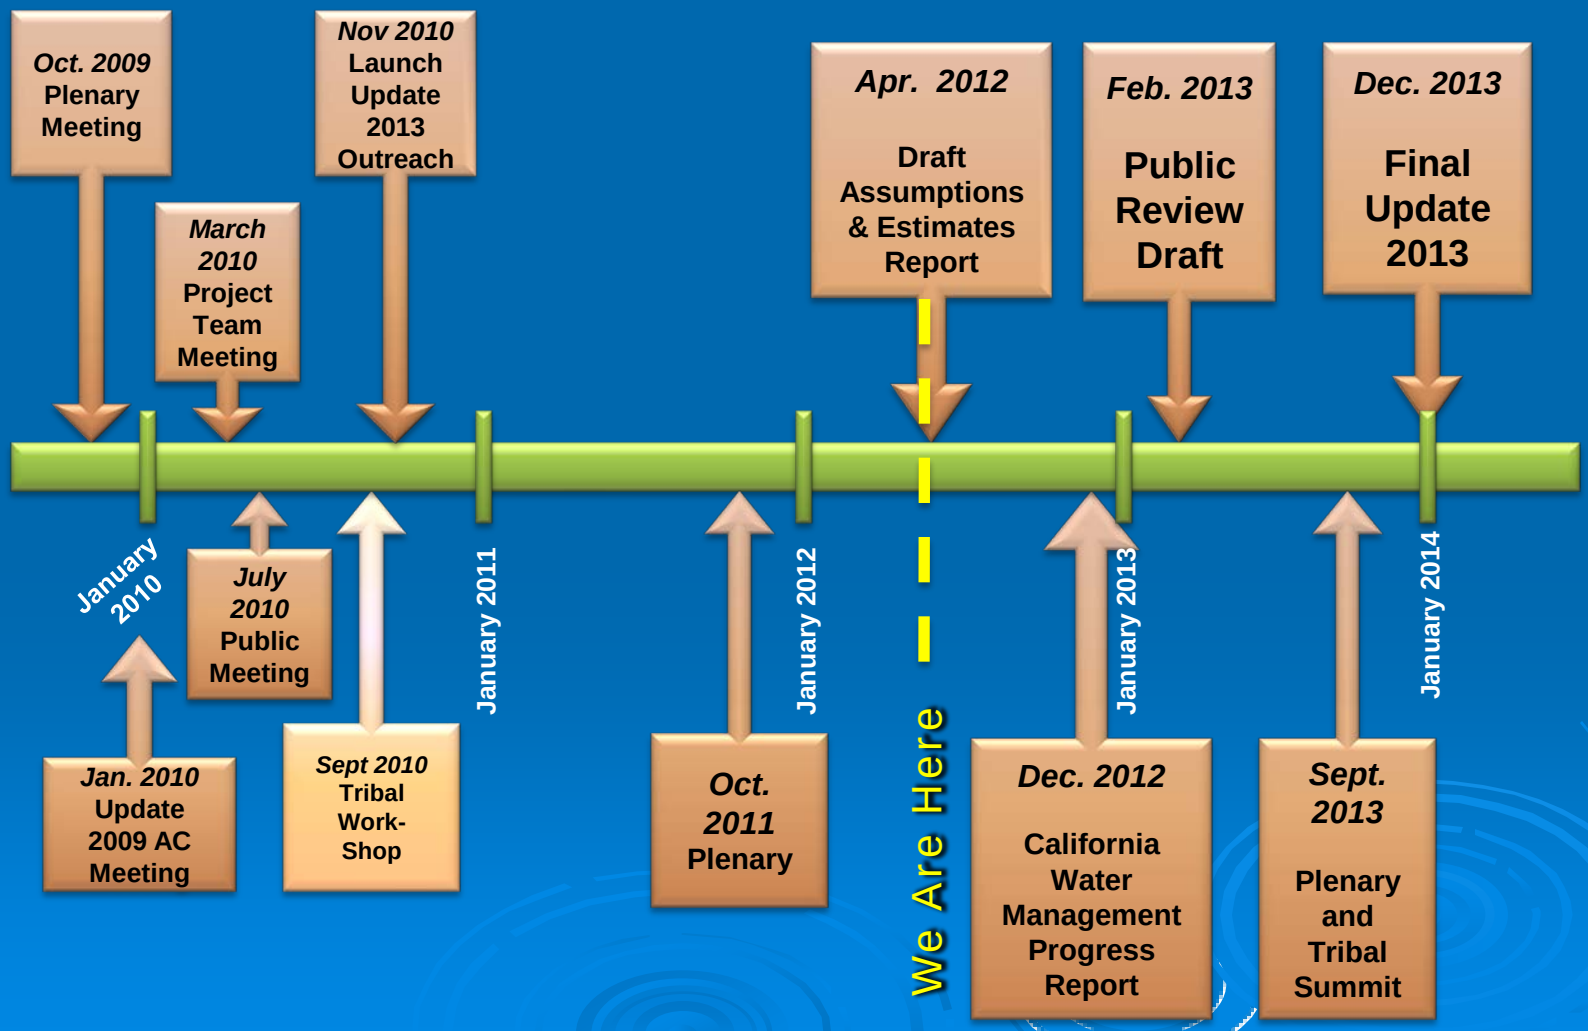

Since our last meeting ….

Outreach and Collaboration

- State Agency Steering Committee meeting
- Mountain Counties Regional Forum
- Scenarios Workshop
- Tribal Advisory Committee meeting
- Three RMS Workshops
  - Outreach and Education
  - Ag Lands Stewardship
  - Sediment Management

Update 2013 Production Schedule For CY 2012

Volume	Chapter/Component	Initial Text Due to Publications (No later than)	Advisory Committee Draft Released	Comments due from Advisory Committee	Volume leads to submit text back to publications staff	Hardstops
1	Introduction	6/1	6/15	10/1	11/1	Admin. Draft to DWR Exec. February 2013 Public Review Draft Release Date April 2013 Final To Governor's Office Sept. 2013 Final Release Dec. 2013
	Policy	8/30	Plenary	10/1	11/1	
	Companion Plans	5/15	6/1	10/1	11/1	
	CA Water Today	6/15	7/1	10/1	11/1	
	Uncertainty	7/15	8/1	10/1	11/1	
	Data and Tools	8/30	Plenary	10/1	11/1	
	Implementation Plan	8/30	Plenary	10/1	11/1	
	Finance Plan	8/30	Plenary	10/1	11/1	
2 Regional Reports	*Staggering will occur, but is largely unforeseeable*	7/1	7/16	9/1	10/1	
3 RMS	*1/2 will come in earlier, 1/3 on time and 3-4 RMSs might not be ready by 5/15*	5/15	6/1	7/1	9/1	
Highlights **	*Text/content submission will be staggered*	10/1	Dec. 13 AC Meeting	12/31	1/31*	

** Highlights will include copy-edit, design and layout for 12/13 AC meeting.

Upcoming Meetings….

❑Ag Water Use Efficiency RMS Workshop	April 5
❑Land Use Caucus	April 5
❑Flood Caucus	April 9
❑Urban Water Use Efficiency RMS Workshop	April 11
❑Salt and Salinity Mgmt. RMS Workshop	April 25
❑Colorado River Regional Forum	April 26
❑Groundwater Caucus	April 27

Upcoming Work

- Release Draft Assumptions and Estimates Report
- Begin writing Volume 1 *[this afternoon]*
- Develop Californians Without Safe Water Report
- Continue updating Resource Management Strategies
- Begin writing Regional Reports
- Form Regional and State Investment Packages for Finance Plan
- Develop template for CA Water Management Progress Report
- Graphics development
